



THE UNITED REPUBLIC OF TANZANIA



PRESIDENT'S OFFICE–PUBLIC SERVICE MANAGEMENT AND GOOD GOVERNANCE

e-Government Authority (e-GA)

Research, Innovation and Development Center (RIDC)

PROJECT PROPOSAL DOCUMENT VERSION 1

October 2026

PROJECT: DAIRE – DECENTRALIZED AI REPUTATION ENGINE

Table Contents

Table Contents.....	2
1. INTRODUCTION.....	5
1.1 Background.....	5
1.2 Problem Statement.....	5
1.3 Purpose of this Proposal.....	5
1.4 Justification.....	6
1.5 Basis of the Proposal.....	6
2. PROJECT OVERVIEW.....	7
2.1 Project Summary.....	7
2.2 Vision.....	7
2.3 Goal and Objectives.....	7
2.3.1 Goal.....	7
2.3.2 Specific objectives.....	7
2.4 Scope.....	8
2.4.1 In scope.....	8
2.4.2 Out of scope.....	8
2.5 Beneficiaries.....	8
2.6 Stakeholders and Responsibilities.....	9
3. PROPOSED SOLUTION.....	10
3.1 Solution Description.....	10
3.2 System Architecture.....	10
3.3 Main Components.....	11
3.4 Business Process Flow.....	11
3.5 Scoring Model.....	11
3.6 Consent and Data Protection by Design.....	12
3.7 Key Features by User.....	12
4. PROJECT APPROACH AND METHODOLOGY.....	13
4.1 Delivery Lifecycle.....	13

4.2 Development Approach.....	13
4.3 Integration Approach.....	13
4.4 Quality Assurance.....	13
4.5 Governance and Reporting.....	14
4.6 Change Management.....	14
5. DELIVERABLES AND EXPECTED OUTCOMES.....	15
5.1 Deliverables.....	15
5.2 Expected Outcomes.....	15
5.3 Key Performance Indicators (proposed).....	15
6. WORK PLAN AND TIMELINE.....	17
6.1 Main Activities.....	17
6.2 Proposed Schedule for the Remaining Work.....	17
6.3 Milestones.....	18
7. RESOURCE REQUIREMENTS AND BUDGET.....	19
7.1 Project Team.....	19
7.2 Infrastructure.....	19
7.3 Budget Estimate.....	19
8. RISK MANAGEMENT.....	21
9. SECURITY, PRIVACY AND COMPLIANCE.....	22
9.1 Security Controls.....	22
9.2 Privacy.....	22
9.3 Compliance.....	22
10. SUSTAINABILITY, MONITORING AND EVALUATION.....	23
10.1 Operations and Support.....	23
10.2 Maintenance.....	23
10.3 Monitoring and Evaluation.....	23
10.4 Handover and Exit.....	23
11. ASSUMPTIONS, DEPENDENCIES AND CONSTRAINTS.....	24

11.1 Assumptions.....	24
11.2 Dependencies.....	24
11.3 Constraints.....	24
12. CONCLUSION AND REQUEST FOR APPROVAL.....	25
Approval.....	25
APPENDIX A: GLOSSARY.....	26
APPENDIX B: REFERENCE DOCUMENTS.....	27
APPENDIX C: PARTICIPATING LENDERS.....	28

1. INTRODUCTION

1.1 Background

Access to credit is one of the main drivers of small business growth, household income and financial inclusion. In Tanzania, many entrepreneurs, women and youth groups and small-scale farmers still cannot obtain a loan from a formal lender because they have no formal credit history. Each Financial Service Provider (FSP) keeps its own customer records, so a person who has repaid loans faithfully at one institution is still treated as an unknown customer by another.

At the same time, the national identity registry (NIDA), the lenders' own core systems and modern technologies such as machine learning and blockchain already exist and can be combined. The e-Government Authority (e-GA), through its Research, Innovation and Development Center (RIDC), proposes the Decentralized AI Reputation Engine (DAIRE) to bring these elements together in one trusted platform.

1.2 Problem Statement

- **No visible credit history** – customers without a formal record are refused credit or pay very high prices for it.
- **Fragmented data** – every lender sees only its own customers, so good repayment behaviour at one lender is invisible to the others.
- **No common trusted identity check** – lenders have no shared and quick way of confirming who the customer is.
- **Inconsistent decisions** – two lenders looking at the same customer may reach different conclusions because they use different evidence.
- **Weak customer control** – customers rarely know which data is shared, with whom and for what purpose.

1.3 Purpose of this Proposal

This document proposes the implementation, testing and roll-out of DAIRE. It describes what will be built, how the work will be organised, what the project will deliver, which resources are needed, which risks must be managed and how success will be measured. It is written for decision makers of the e-GA and of the participating institutions so that they can review and approve the project.

1.4 Justification

Need	How DAIRE responds
Include customers without a credit history	Builds a score from verified behaviour data (accounts, transactions, loans and repayments) instead of requiring a prior credit file
Reduce lender risk	One score from five weighted dimensions, with clear risk bands, shown to every lender
Consistent decisions	The identical result is broadcast to all lenders linked to the customer
Trust in identity	Every customer is verified against NIDA before activation
Protect the customer	Data is shared only after consent, which the customer can withdraw
Transparency and auditability	Scores are recorded on a blockchain contract and every exchange is logged

1.5 Basis of the Proposal

The proposal builds on work that has already been carried out: the Software Requirements Specification (SRS), the System Design Document (SDD) with nine diagrams, the DAIRE Work Plan and the Software Testing Document (STD), as well as working components of the NIDA service, the lender systems, the Central System, the AI engine and the blockchain contract. These documents are listed in Appendix B.

2. PROJECT OVERVIEW

2.1 Project Summary

Item	Description
Project title	DAIRE – Decentralized AI Reputation Engine
Proposed by	e-Government Authority (e-GA), Research, Innovation and Development Center (RIDC)
Participating institutions	CRDB (CRDB-01), Ministry of Finance lender (MoFinance-004), NMB (NMB-01 and NMB-02), NIDA
Project type	Software development, integration, testing and roll-out
Output	A shared credit reputation score (300 to 850) delivered to all linked lenders
Main technologies	Django / Django REST Framework, PostgreSQL, Angular, scikit-learn, Solidity smart contract, Node.js (Express), Hardhat
Proposed duration	To be agreed; see Chapter 6
Estimated budget	To be completed; see Section 7.3

2.2 Vision

Every Tanzanian who behaves responsibly with money can prove it and be offered fair credit, whichever lender they approach.

2.3 Goal and Objectives

2.3.1 Goal

To provide a trusted, shared and consent-based credit reputation service for lenders in Tanzania.

2.3.2 Specific objectives

1. Verify every customer against NIDA before an account is activated.
2. Connect the lender systems of CRDB, the Ministry of Finance and NMB to one Central System.
3. Merge a customer's records from all lenders into one profile using a single borrower reference.
4. Calculate one credit score between 300 and 850 using an AI reputation model and a blockchain contract.
5. Return the identical result to every linked lender so that all decisions rest on the same evidence.
6. Give customers control through consent that can be granted, extended and revoked.
7. Provide administrators with monitoring, routing policies and a complete audit trail.
8. Prove the quality of the system through a planned test programme and a formal acceptance.

2.4 Scope

2.4.1 In scope

- NIDA identity verification service and its read-only citizen view
- Lender back-ends and Angular user interfaces for customers and staff
- Central System with an Angular operations console
- AI reputation engine (Random Forest model, with a fallback formula)
- DaireCreditScore smart contract and its Express middleware
- Broadcast of results to all linked lenders
- Documentation (SRS, SDD, STD, work plan), training and handover

2.4.2 Out of scope

- Changes to the internal core banking systems of the lenders beyond the agreed interfaces
- Mobile network operator and payment gateway integration
- A public credit bureau licence or regulatory approval, which remain with the institutions concerned
- Marketing campaigns for customers

2.5 Beneficiaries

Group	Benefit
Customers (entrepreneurs, women and youth groups, small-scale farmers)	Fair access to credit based on their own behaviour; control over data sharing
Lenders	Lower risk, faster and consistent decisions, reach to new customers
e-GA and Government	A reusable digital public infrastructure for trusted data sharing
NIDA	A controlled, audited use of its identity verification service
Regulators	Transparent, auditable scoring and data exchange

2.6 Stakeholders and Responsibilities

Stakeholder	Responsibility
e-GA / RIDC	Project owner; design, development, testing coordination, hosting and support
NIDA	Provides the identity verification service and approves trusted client addresses
CRDB	Provides test and live access to its lender system; nominates focal persons
Ministry of Finance (MoFinance-004)	Provides lender system access and focal persons
NMB	Provides access to NMB-01 and NMB-02; nominates focal persons
Steering Committee	Approves scope, budget changes and acceptance
Test Team and QA	Executes the Software Testing Document and reports results

3. PROPOSED SOLUTION

3.1 Solution Description

DAIRE connects the systems of the lenders to one Central System. A customer is first verified against NIDA. With the customer's consent, each lender sends its data (accounts, transactions, loans and repayments) to the Central System, which merges the records using a single borrower reference. An AI reputation model and a blockchain smart contract analyse the merged record and produce one score between 300 and 850. The identical result is then broadcast to every lender linked to that borrower.

3.2 System Architecture

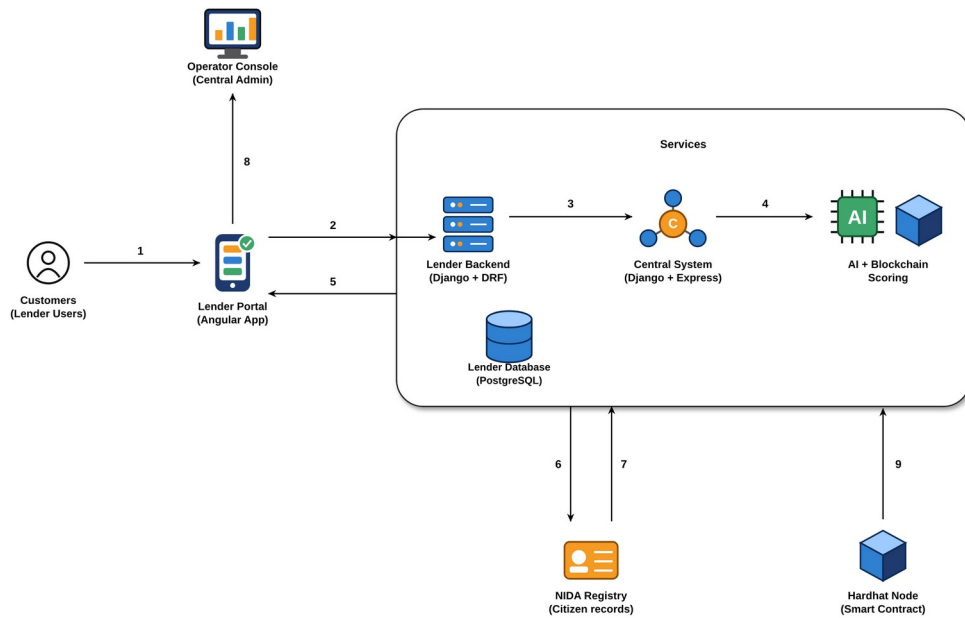


Figure 1: DAIRE system architecture

3.3 Main Components

Component	Function	Technology
NIDA service	Verifies a citizen by NIDA number and personal details; health check	Django, DRF, PostgreSQL
Lender systems	Customer sign-up, accounts, transactions, loans, consent, push of data and receipt of results	Django 4.2, DRF 3.15, JWT; Angular
Central System	Receives and merges lender data, runs assessments, applies routing policies, broadcasts results	Django 5.2, DRF, PostgreSQL; Angular console
AI engine	Generates 11 credit features and returns a reputation result	scikit-learn Random Forest (joblib)
Blockchain contract	Calculates and stores the five-dimension score and risk band	Solidity, Hardhat
Express middleware	Submits features to the contract and reads stored scores	Node.js, Express

3.4 Business Process Flow

1. The customer is verified against NIDA and the account is activated with a one-time password (valid for 10 minutes) and a 4-digit PIN.
2. The customer uses the lender's services; accounts, transactions, loans and repayments are recorded.
3. The customer grants consent for data to be shared with the Central System.
4. The lender pushes the consented data to the Central System, which merges it by borrower reference.
5. The Central System requests the AI reputation result and the blockchain score.
6. The Central System broadcasts the identical result to every lender linked to the borrower.
7. The lender officer sees the score and band when deciding on a loan application.

3.5 Scoring Model

The blockchain contract scores five dimensions from 0 to 100. Their weights follow international practice (FICO and VantageScore) and are adjusted for Tanzania, where mobile money activity can show financial stability for customers who have never had a bank loan.

ID	Dimension	Weight
D1	Payment Reliability	30%
D2	Financial Stability	20%
D3	Credit and Debt Management	15%
D4	Behavioural Consistency	20%
D5	Verified Trust Evidence	15%

The score is 300 plus the weighted sum multiplied by 550 and divided by 10,000. The score maps to five risk bands. If any dimension is below 40, the band cannot be better than Fair.

Band	Score range
Poor	below 580
Fair	580 – 669
Good	670 – 739
Very Good	740 – 799
Exceptional	800 and above

3.6 Consent and Data Protection by Design

- Data is pushed to the Central System only after the customer has granted consent; revoking consent stops further pushes.
- Identity details (NIDA number, name, phone) are not sent to the AI engine.
- The AI inputs are kept so that each result can be reviewed.
- Access is limited by IP allow-lists, optional API keys and role-based permissions.
- Every data exchange and administrator action is written to the audit log.

3.7 Key Features by User

User	Main features
Customer	Sign-up with NIDA, login with OTP, accounts and transactions, loan application, consent control, credit score and history, notifications
Loan officer	View and decide on applications, see the central score and band, view repayment schedules
Lender administrator	Customers and accounts, system settings, lender credentials, audit logs
Central administrator	Lenders registry, routing policies, data exchanges, assessments, dashboard and audit logs

4. PROJECT APPROACH AND METHODOLOGY

4.1 Delivery Lifecycle

The project follows the document flow used by the e-GA: requirements first, then design, then development, then a planned test programme, and finally deployment and handover. Each stage produces a document that is reviewed before the next stage begins.

Stage	Activities	Document / Output
1. Requirements	Study the lenders, NIDA and the data needed; agree functions and rules	Software Requirements Specification (SRS)
2. Design	Architecture, data flow, database, use cases and sequence diagrams	System Design Document (SDD) and nine diagrams
3. Planning	Activities, owners and status tracking	DAIRE Work Plan (Excel)
4. Development	Build NIDA, lender, Central, AI and blockchain components; integrate them	Working software
5. Testing	Execute the planned test cases and correct defects	Software Testing Document (STD) and test reports
6. Deployment	Install on production servers, load lenders, go live in stages	Deployment record
7. Handover	Training, operation manuals, support arrangement	Training material and handover certificate

4.2 Development Approach

- Short iterations of build, review and test, with demonstrations to the lenders after each iteration
- Components developed independently and connected through documented interfaces (REST APIs)
- Source control and code review for every change
- Automated tests for critical rules such as the score formula and band boundaries

4.3 Integration Approach

Integration is done in this order: lender to NIDA, lender to Central System, Central System to the AI engine, Central System to the blockchain middleware, and Central System back to the lenders. Each connection is proven with the integration test cases before the next is started. Lenders are connected one at a time, beginning with CRDB, then NMB, then the Ministry of Finance lender.

4.4 Quality Assurance

Quality is assured through the Software Testing Document, which contains 164 designed test cases in 15 modules covering NIDA, authentication, banking, loans, consent, integration, the Central System, AI, blockchain, broadcast, administration, user interface, security, performance and end-to-end scenarios. Exit criteria are given in the STD.

4.5 Governance and Reporting

Mechanism	Frequency	Participants
Progress report	Every two weeks	Project Manager to Steering Committee
Working meeting	Weekly	e-GA team and lender focal persons
Steering Committee	Monthly or at milestones	e-GA, NIDA and lender executives
Test status report	Daily during testing	Test Manager to Project Manager

4.6 Change Management

Any change to scope, schedule or cost is written as a change request, assessed for effect on the work plan and budget, and approved by the Steering Committee before work begins.

5. DELIVERABLES AND EXPECTED OUTCOMES

5.1 Deliverables

No.	Deliverable	Status
1	Software Requirements Specification (SRS), 115 pages	Delivered
2	System Design Document (SDD), 52 pages	Delivered
3	Nine design diagrams (architecture, flowchart, data flow, ERD, use case and four sequence diagrams)	Delivered
4	DAIRE Work Plan (Excel)	Delivered
5	Software Testing Document (STD), 164 test cases	Delivered; tests not yet run
6	NIDA service with verification API and citizen view	Developed; to be tested
7	Lender systems and user interfaces (CRDB, NMB and MoFinance)	Developed; to be tested; MoFinance details to be confirmed
8	Central System and operations console	Developed; to be tested
9	AI reputation engine	Developed; to be tested
10	Blockchain contract and middleware	Developed; to be tested
11	Test reports and acceptance certificate	Planned
12	Operation manuals and training	Planned

Status of items 6 to 10 is taken from the present state of the work plan and must be confirmed by the project team.

5.2 Expected Outcomes

- Customers without a formal history receive a credible score from verified behaviour data.
- All linked lenders see the same score and risk band for the same customer.
- Loan decisions become faster and more consistent.
- Customers control which data is shared and can withdraw consent.
- The e-GA owns a reusable platform for trusted, auditable data sharing between institutions.

5.3 Key Performance Indicators (proposed)

The targets below are proposals for discussion; baseline values must be measured before go-live.

Indicator	Proposed target
Test cases passed before go-live	At least 90% passed; no open Critical or High defect
Identical score delivered to every linked lender	100% of broadcasts
Score request response time	95% within 3 seconds (to be agreed)
Lenders connected	4 (CRDB-01, MoFinance-004, NMB-01, NMB-02)
Customers with a score after six months	Target to be set with lenders
Share of loan applications that use the DAIRE score	Target to be set with lenders

6. WORK PLAN AND TIMELINE

6.1 Main Activities

The detailed plan is in the DAIRE Work Plan (Excel). The table summarises the main activities and their present state as recorded there.

Main activity	Content	State
Requirements and design	SRS; SDD with diagrams	Completed
NIDA system	Citizen database, verification API, IP allow-list, read-only role and view	Completed
Lender back-end	Authentication, banking, loans, consent, DAIRE integration, settings and audit	Completed
Lender front-end	Customer portal and administration portal for CRDB and NMB	Completed
Central System	Lenders, data receive and merge, routing, assessments, broadcast, console	Completed
AI engine	Feature generation, model integration, fallback formula	Completed
Blockchain	Smart contract, middleware, node deployment	Completed
Integration	Lender–NIDA, lender–Central, Central–AI, Central–blockchain; all four lenders end to end	End-to-end for all lenders not completed
Testing	Execution of 164 test cases and correction of defects	Not started
Deployment and handover	Production install, training, manuals, acceptance	Not started

States are inferred from the project and must be confirmed by the team.

6.2 Proposed Schedule for the Remaining Work

Phase	Activity	Duration (proposed)
1	Environment setup, data load and smoke test	3 days
2	Test NIDA, authentication, banking, loans and consent	5 days
3	Test integration, Central System, AI, blockchain, broadcast and administration	7 days
4	Test interface, security and performance	5 days
5	End-to-end scenarios and regression	4 days
6	User acceptance and sign-off	3 days
7	Production deployment, staged lender go-live, training and handover	To be agreed

Testing alone is estimated at 27 working days. Start dates depend on access to the lender and NIDA environments and are to be agreed.

6.3 Milestones

Milestone	Evidence
M1 Requirements and design approved	SRS and SDD signed
M2 Components ready for test	Smoke test passed
M3 Integration complete	All integration test cases passed
M4 System test complete	Exit criteria of the STD met
M5 User acceptance	Acceptance sign-off by e-GA and lenders
M6 Go-live and handover	Production running; training completed

7. RESOURCE REQUIREMENTS AND BUDGET

7.1 Project Team

Role	Responsibility	Number
Project Manager	Plans, tracks and reports	[]
Business Analyst	Requirements and acceptance support	[]
Back-end Developers	Django services, integration, AI interface	[]
Front-end Developers	Angular interfaces	[]
Blockchain Developer	Smart contract and middleware	[]
Data Scientist	AI model, features, monitoring	[]
Test Engineers	Execute the STD	[]
DevOps / System Administrator	Servers, databases, deployment, monitoring	[]
Security Officer	Security review and testing	[]

Numbers are left open to be set by e-GA management.

7.2 Infrastructure

Item	Requirement
Servers	Linux server or virtual machine for each of NIDA, Central System, blockchain node and each lender (4 CPU, 8 GB RAM, 50 GB disk as a starting size)
Database	PostgreSQL for NIDA, Central System and each lender
Network	Private network between institutions, with allow-listed addresses; HTTPS for all interfaces
Test environment	Separate from production, with fictitious test data
Tools	Source control, issue tracker, API test tools, load testing tool, monitoring

7.3 Budget Estimate

No cost figures have been provided for this proposal. The table gives the cost categories to be completed by e-GA finance and procurement.

No.	Cost category	Amount (TZS)
1	Personnel (project team)	[]
2	Servers and hosting	[]
3	Software licences and tools	[]
4	Testing (including security testing)	[]
5	Training and manuals	[]
6	Travel and workshops with lenders	[]
7	Support and maintenance (first year)	[]
8	Contingency	[]
	Total	[]

8. RISK MANAGEMENT

Risk	Likelihood	Impact	Mitigation
Lender or NIDA test access delayed	Medium	High	Agree access and focal persons at the start; escalate to the Steering Committee
Poor data quality from lenders	Medium	High	Validation on receipt; conflict recording; data quality checks with lenders
Customer consent not given or withdrawn	Medium	Medium	Clear consent screens; respect revocation at once
AI model gives unstable scores	Low	High	Fix model version; fallback formula; monitor drift
Blockchain node reset or loss of history	Low	High	Redeploy procedure; backups of submitted features; permanent node in production
Security breach or misuse of data	Low	High	Allow-lists, API keys, tokens, audit logs, security testing
Scope growth	Medium	Medium	Change control through the Steering Committee
Slow response under load	Medium	Medium	Performance tests; capacity planning
Key staff leave	Low	Medium	Documentation; knowledge sharing; handover

9. SECURITY, PRIVACY AND COMPLIANCE

9.1 Security Controls

- Customer identity is checked against NIDA before activation.
- Login uses account number, hashed 4-digit PIN and a 10-minute one-time password.
- JWT access tokens last 12 hours and refresh tokens 7 days.
- NIDA accepts calls only from trusted client addresses; lenders accept callbacks only from trusted callback addresses.
- API keys can be required for lender and Central System interfaces.
- The NIDA reader role is read-only.
- Transport security (HTTPS) is required in production.

9.2 Privacy

- Data is shared only with consent, for the categories the customer has selected, and for a period the customer can see.
- Only the data needed for scoring is sent; identity details are not sent to the AI engine.
- Customers can view and revoke consent and see their score and history.

9.3 Compliance

The project will follow the e-GA standards and guidelines and the data protection law in force in Tanzania. The legal basis for sharing data between institutions, and any licence needed to operate a credit reputation service, must be confirmed by the legal advisers of the participating institutions before go-live.

10. SUSTAINABILITY, MONITORING AND EVALUATION

10.1 Operations and Support

- A support desk at the e-GA receives incidents from lenders and customers.
- Defects are classified by severity as in the Software Testing Document (Critical, High, Medium, Low).
- Monitoring of servers, interfaces and the dashboard of the Central System.

10.2 Maintenance

- Regular updates of frameworks and libraries
- Periodic review of the AI model and of the dimension weights
- Regression testing after each change
- Backups of databases and of submitted features

10.3 Monitoring and Evaluation

What is measured	How	When
Progress against the work plan	Work Plan status review	Every two weeks
Quality	Test results and defect counts	During testing
Service use	Dashboard of exchanges and assessments	Monthly
Outcomes	Indicators in Section 5.3	Quarterly after go-live
Customer experience	Feedback from customers and lenders	Quarterly

10.4 Handover and Exit

At the end of the project the e-GA receives source code, documents, manuals and access credentials, and the lender teams and administrators are trained. A handover certificate is signed by the project owner.

11. ASSUMPTIONS, DEPENDENCIES AND CONSTRAINTS

11.1 Assumptions

- The SRS and SDD form the agreed baseline.
- The lenders and NIDA will provide test and production access on time.
- Test data is fictitious or anonymised.
- Details of the Ministry of Finance lender (address and credentials) will be supplied.

11.2 Dependencies

- Availability of the NIDA service and of its trusted client address list
- Participation of lender focal persons
- Approval of budget and staff by the e-GA

11.3 Constraints

- Systems run on private networks; access must be arranged before testing.
- Real customer data must not be used for testing.
- Performance targets and schedules are proposals until approved.

12. CONCLUSION AND REQUEST FOR APPROVAL

DAIRE answers a clear need: to give people without a formal credit history a fair chance of credit, and to give lenders one trusted view of the customer. The requirements, design, work plan and test plan are complete, and the main components have been developed. What remains is to confirm the open items, run the test programme, connect all lenders end to end, and deploy.

The Steering Committee is requested to:

1. Approve this project proposal and its scope.
2. Approve the budget once the categories in Section 7.3 are completed.
3. Nominate focal persons from NIDA, CRDB, the Ministry of Finance and NMB.
4. Approve the schedule for the testing and acceptance programme.

Approval

Name	Role	Signature	Date
	Project Owner, e-GA		
	Director, RIDC		
	NIDA Representative		
	CRDB Representative		
	Ministry of Finance Representative		
	NMB Representative		

APPENDIX A: GLOSSARY

Term	Meaning
DAIRE	Decentralized AI Reputation Engine
e-GA	e-Government Authority
RIDC	Research, Innovation and Development Center
FSP	Financial Service Provider
NIDA	National Identification Authority
OTP	One-Time Password
PIN	Personal Identification Number
JWT	JSON Web Token
API	Application Programming Interface
SRS	Software Requirements Specification
SDD	System Design Document
STD	Software Testing Document
Borrower reference	Single reference used to merge a borrower's records from all lenders
Smart contract	A program stored on a blockchain that runs the same way every time
Random Forest	A machine learning method that combines many decision trees

APPENDIX B: REFERENCE DOCUMENTS

Document	Description
DAIRE SRS Version 1	Functional and non-functional requirements
DAIRE SDD Version 1	Architecture, data design, interface design and diagrams
DAIRE SDD Diagrams	Nine diagrams as images
DAIRE Work Plan	Excel work plan with activity status
DAIRE STD Version 1	Test strategy and 164 test cases
Central System documents	AI_DATA_CONTRACT.md, LENDER_SUBSYSTEM_README.md, STEP-02-SCORING.md
Smart contract	DaireCreditScore.sol

APPENDIX C: PARTICIPATING LENDERS

Lender	Code	Notes
CRDB	CRDB-01	User interface on port 4600; back-end on port 8002
Ministry of Finance	MoFinance-004	Same lender sub-system; address to be confirmed
NMB	NMB-01, NMB-02	User interface on port 4300; back-end on port 8002
